


Company: _____

Address (where the system is installed): _____

Datum: _____

Checkpoints

Check the boxes after each check performed:

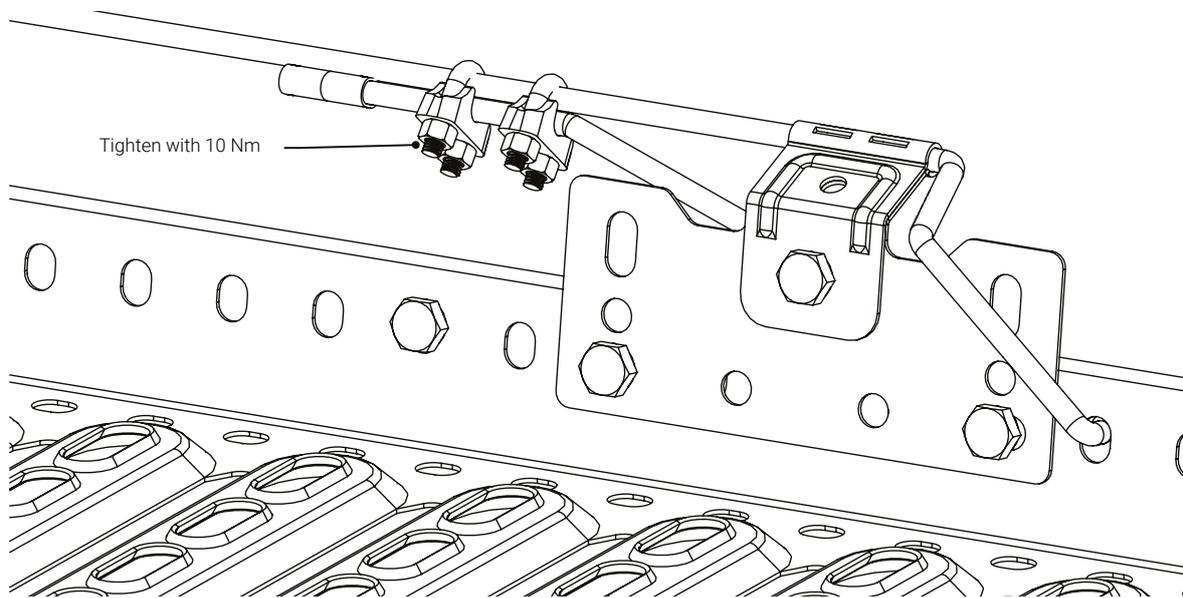


- Check that the wire lock is tightened with the correct torque, wire lock is tightened with 10 Nm.
- Check that the wire is intact. If the wire is damaged in the form of jacks or broken wires, the wire must be replaced.
- Check that the wire is tightened correctly (see page 2).
- Check that all bolts and nuts are tightened.

INSPECTION CARRIED OUT BY


Company/Organisation: _____

Name: _____


Place and date: _____

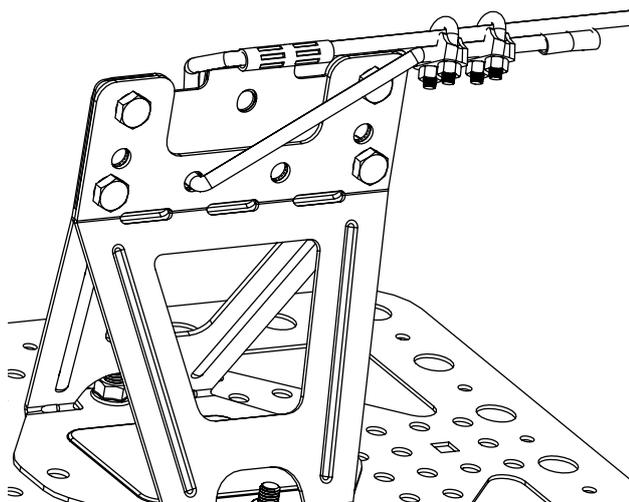


Weline ONE on flat roofs

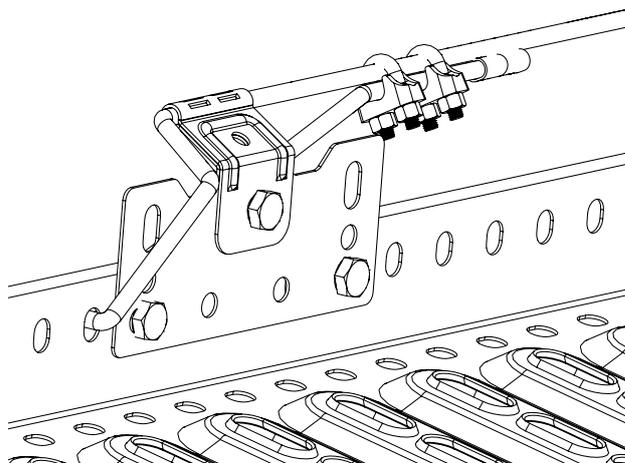


Weline ONE on roof bridge

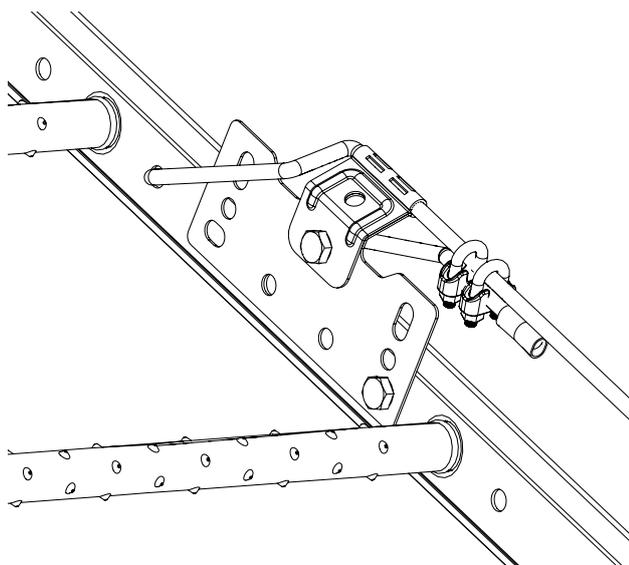

Weline ONE on roof ladder

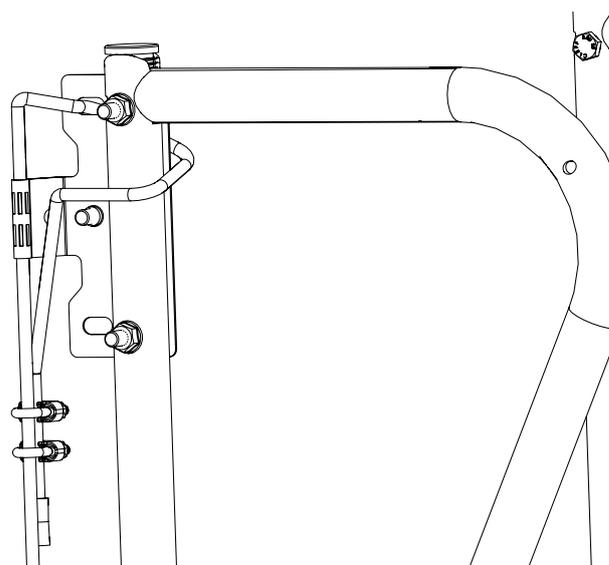

Weline ONE on facade ladder



Weline ONE on ridge rail
